



# COMMUNITY PROJECTS MONTHLY UPDATE

## Fiscal Year 2021-22 Discretionary Fund Projects

Public Works Department  
September 15, 2023



# TABLE OF CONTENTS

MONTHLY PROGRESS UPDATE_____	3
Background _____	3
PROJECTS IN CONSTRUCTION_____	3
Brooking, Panella, Sandman & Weber Park Playground Replacements, Project No. WP22026 _____	3
Citywide Park Walkway Replacement, Project No. WT22015 _____	4
Downtown Decorative Streetlight LED Conversion, Project No. WD22016 _____	5
Intersection Safety Tree Trimming, Project No. WD22018 _____	6
Miracle Mile RRFB & Improvements, Project No. WT22052 _____	6
Pixie Woods Improvements, Project No. WP22054 _____	7
Sidewalk Replacements, Project No. WD22053 _____	7
Swimming Pool UV Sterilization System Improvements, Project No. WP22027 _____	7
Tree Maintenance, Project No. WE22052 _____	8
Van Buskirk Gym Floor Replacement, Project No. WC22003 _____	8
Victory Park Tennis Court Lighting Refurbishment, Project No. WP22030 _____	9
Weber Point Events Center Shade Structure Rehab, Project No. WP22033 _____	9
PROJECTS IN DESIGN _____	9
American Legion Park Lagoon Fencing Replacement, Project No. WP22036 _____	9
Citywide Bridge Slope Protection, Project No. WT22039 _____	9
Grupe Park Parking Lot Resurfacing, Project No. WD22011 _____	9
Mattie Harrell Park Irrigation Well Replacement, Project No. WP22037 _____	9
Oak Park Senior Center Parking Lot Resurfacing, Project No. WD22012 _____	10
Pixie Woods Irrigation Automation, Project No. WP22038 _____	10
Sousa Pool Crack Repair and Re-plastering, Project No. WP22040 _____	10
Teen Impact Center Rehabilitation, Project No. CR22001 _____	10
PROJECTS COMPLETED _____	10
Downtown Abandoned Meter Pole Removals, Project No. WD22015 _____	10
Fire Station 1 Renovations, Project No. F022002 _____	10
Five Mile Creek Hyacinth Removal, Project No. WC22005 _____	11
Gospel Center Rescue Mission Sidewalk Replacement, Project No. WD22017 _____	11
Lower Sac Road Bridge at Mosher Slough Fence, Project No. WD22010 _____	11
Oak Park Ball Field Improvements, Project No. WP22055 _____	11
Pixie Woods Suspension Bridge Replacement, Project No. WP22039 _____	11
Pixie Woods Tree Trimming & Brush Removal, Project No. WP22013 _____	11
Stockton Soccer Complex Playground & Food Truck Pad, Project No. CR15010 _____	11
Teen Impact Center Roof Replacement & Repairs, Project No. CR22002 _____	11
Waterfront Lighting Restoration, Project No. WD22014 _____	11
FINANCIAL SUMMARY _____	12

# MONTHLY PROGRESS UPDATE

## Background

This monthly report is to provide a brief progress update on the multiple discretionary funded projects approved by City Council on November 16, 2021, by Resolution No. 2021-11-16-1501. Council allocated \$9.85 million in funding for various park, tree, transportation, and facility improvement projects citywide for delivery by the Public Works Department.

On May 3, 2022, by Resolution No. 2022-05-03-0903, Council allocated an additional \$10.2 million in funding for projects including sidewalk replacements, tree maintenance, and park improvements.

## PROJECTS IN CONSTRUCTION

### Brooking, Panella, Sandman & Weber Park Playground Replacements, Project No. WP22026

A recommendation to award Brooking, Panella, and Weber playground replacements is tentatively scheduled for the September 26 City Council meeting.

A public outreach meeting for the all-abilities playground at Sandman Park was held on August 7. The comments from the meeting are being incorporated into the final design and the award of the contract for Sandman Park is expected by December 2023.



*Overall Construction Completion ..... 0%*



## Citywide Park Walkway Replacement, Project No. WT22015

Project includes evaluating trip hazards at multiple community park sites, such as Victory, Faklis, Weston, Sherwood, and more. Repairs were completed at Faklis, Weston, and Sherwood Parks last month. Repairs at Victory Park commence next week.




Overall Construction Completion ..... 65%



## Downtown Decorative Streetlight LED Conversion, Project No. WD22016

This project is now complete with over 350 decorative Downtown streetlights converted to LED fixtures.

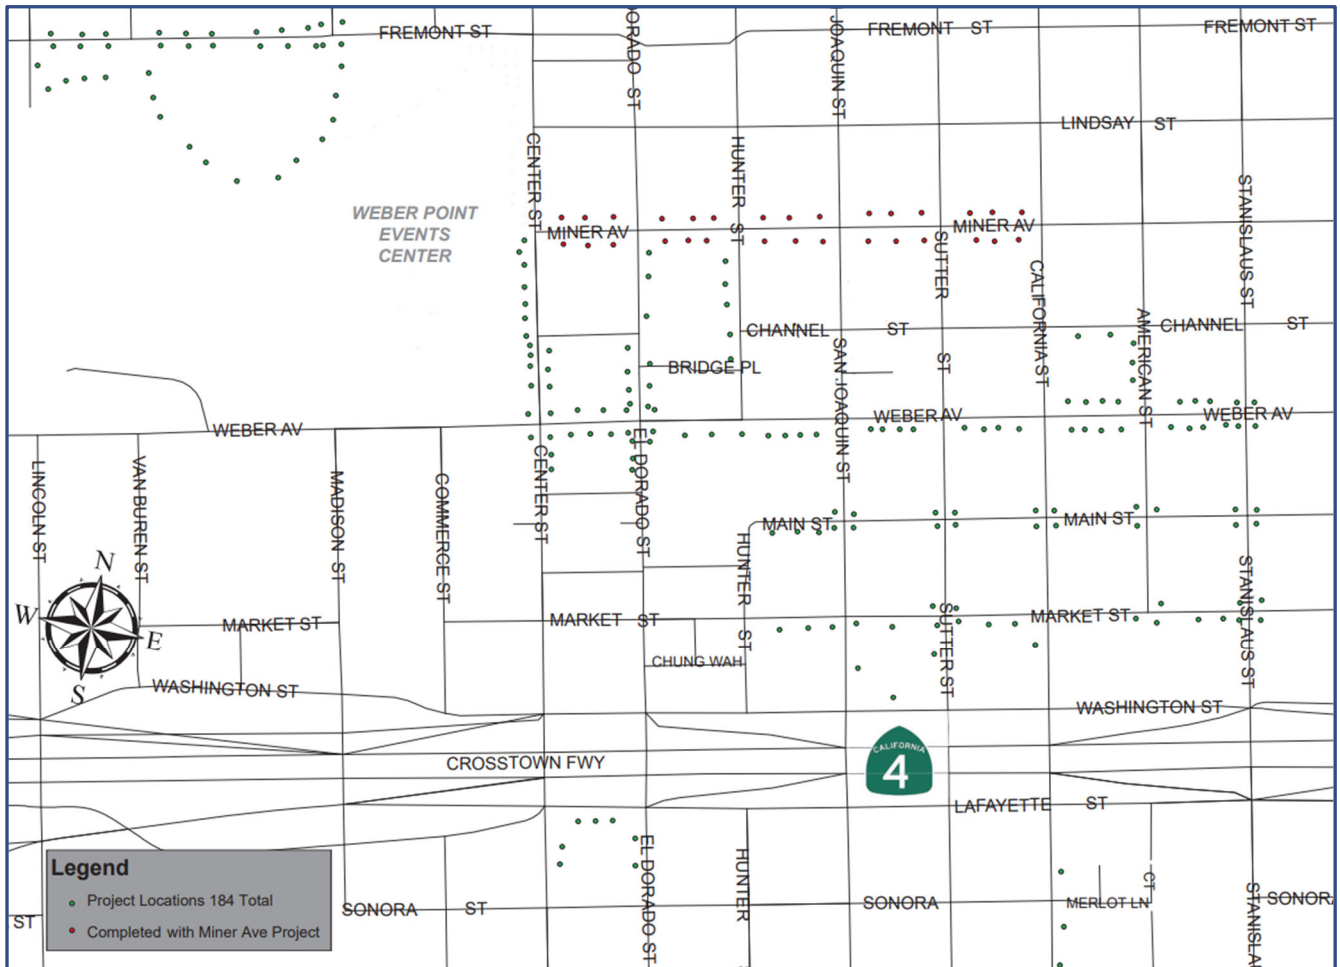

Overall Construction Completion ..... 100%


## Intersection Safety Tree Trimming, Project No. WD22018

The Construction Contract was awarded at the June 20 City Council meeting. A public outreach plan is being finalized prior to the Contractor starting work in October.

*Overall Construction Completion* ..... 0%

## Miracle Mile RRFB & Improvements, Project No. WT22052

The Construction Contract was awarded at the August 22 City Council meeting. Work is anticipated to begin in October and be completed by the end of December, weather permitting.

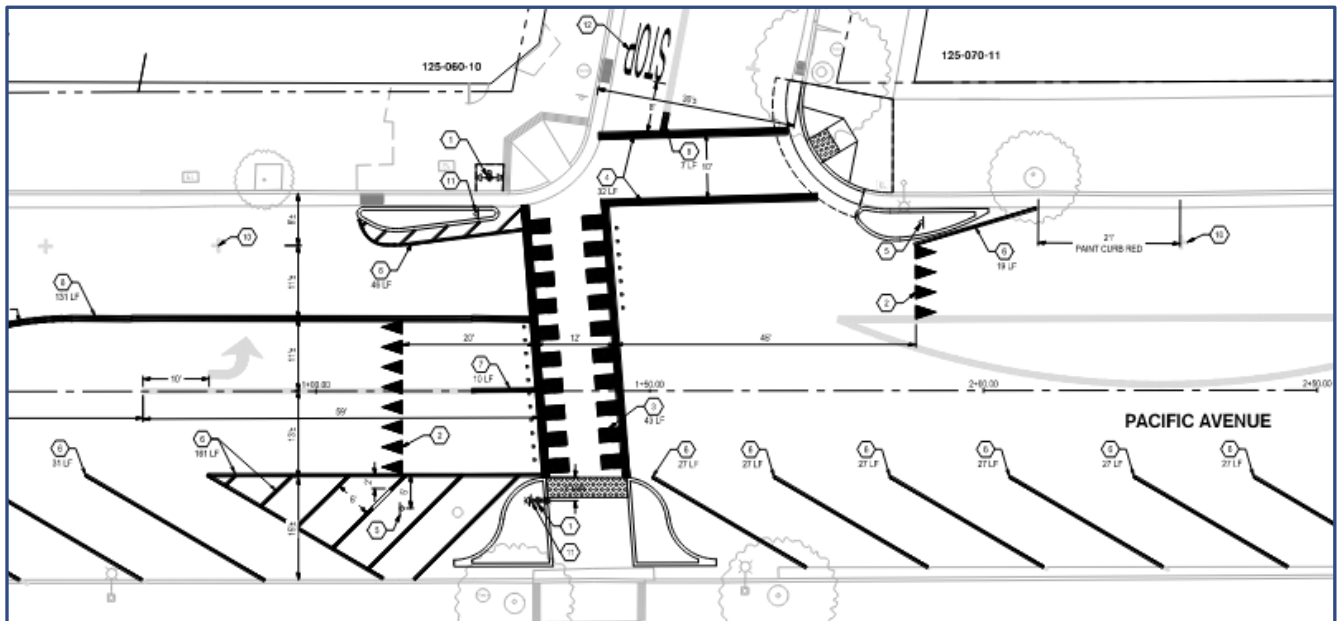

*Overall Construction Completion* ..... 0%



### Pixie Woods Improvements, Project No. WP22054

Public Works and Community Services Departments met with the Pixie Woods Board in summer of 2022 to identify and prioritize improvements. Additional carousel repairs are underway with fabrication of replacement components. The custom cranks and hi hats were received (photos below) and will be installed later this September.



*Overall Construction Completion* ..... 25%

### Sidewalk Replacements, Project No. WD22053

The tree removal component of this project was awarded a Construction Contract at the March 21 City Council meeting. The project has been suspended indefinitely.

*Overall Construction Completion* ..... 60%

### Swimming Pool UV Sterilization System Improvements, Project No. WP22027

Staff recommends a scope change to assess the needs of existing aquatic facilities and to prioritize improvements to better serve the needs of the community. Emergency repairs at

Brooking Pool were recently completed and staff will be ratifying the repairs before City Council for approval at the October 17 meeting.



*Overall Construction Completion ..... 100%*

#### **Tree Maintenance, Project No. WE22052**

The Construction Contract was awarded at the June 20 City Council meeting. A public outreach plan is being finalized prior to the Contractor starting work in October.

*Overall Construction Completion ..... 0%*

#### **Van Buskirk Gym Floor Replacement, Project No. WC22003**

HY Flooring began applying the AC-Tech epoxy to the gym floor last week. Photos below.



*Overall Construction Completion ..... 35%*



### **Victory Park Tennis Court Lighting Refurbishment, Project No. WP22030**

Long lead material items have been ordered by the Contractor. The Contractor expects delivery of the electrical pedestal by mid-October with improvements immediately following.

*Overall Construction Completion ..... 0%*

### **Weber Point Events Center Shade Structure Rehab, Project No. WP22033**

Bid opening was on August 31 and one bid was received. The bid is regular and will be recommended for approval at the November City Council meeting.

*Overall Construction Completion ..... 15%*

## **PROJECTS IN DESIGN**

### **American Legion Park Lagoon Fencing Replacement, Project No. WP22036**

Construction is anticipated to start in November 2023.

*Overall Design Completion ..... 50%*

### **Citywide Bridge Slope Protection, Project No. WT22039**

Slope protection at Airport Way and Mormon Slough is scheduled to be complete with design early 2024 and be in construction by the following summer.

*Overall Design Completion ..... 65%*

### **Grupe Park Parking Lot Resurfacing, Project No. WD22011**

Design is wrapping up and the project is scheduled to advertise for construction bids this month with bid opening in November. Construction is anticipated to take place in early spring 2024.

*Overall Design Completion ..... 99%*

### **Mattie Harrell Park Irrigation Well Replacement, Project No. WP22037**

The project is scheduled to advertise for bids in early 2024.

*Overall Design Completion ..... 10%*

### **Oak Park Senior Center Parking Lot Resurfacing, Project No. WD22012**

Design is wrapping up and the project is scheduled to advertise for construction bids this month with bid opening in November. Construction is anticipated to take place in early spring 2024.

*Overall Design Completion..... 99%*

### **Pixie Woods Irrigation Automation, Project No. WP22038**

The irrigation master plan evaluation and design are complete. The project is scheduled to advertise for construction bids in October.

*Overall Design Completion..... 99%*

### **Sousa Pool Crack Repair and Re-plastering, Project No. WP22040**

An assessment was completed in December with final recommendations for pool improvements. Replastering will be scheduled at close of the 2023 operating season. It is recommended that a strategic plan be prepared to address the repairs needed at this facility, as well as others, to better serve the needs of the community.

*Overall Design Completion..... 99%*

### **Teen Impact Center Rehabilitation, Project No. CR22001**

This facility is being evaluated for different operations and best uses. Economic Development will include this facility in an upcoming RFP to seek interest in City-owned sites and facilities (surplus properties) in the greater Downtown footprint.

*Overall Design Completion..... 5%*

## **PROJECTS COMPLETED**

### **Downtown Abandoned Meter Pole Removals, Project No. WD22015**

Completed November 2022.

### **Fire Station 1 Renovations, Project No. F022002**

Completed April 2023.



**Five Mile Creek Hyacinth Removal, Project No. WC22005**

Completed March 2022.

**Gospel Center Rescue Mission Sidewalk Replacement, Project No. WD22017**

Completed May 2023.

**Lower Sac Road Bridge at Mosher Slough Fence, Project No. WD22010**

Completed January 2023.

**Oak Park Ball Field Improvements, Project No. WP22055**

Completed March 2023.

**Pixie Woods Suspension Bridge Replacement, Project No. WP22039**

Completed April 2023.

**Pixie Woods Tree Trimming & Brush Removal, Project No. WP22013**

Completed November 2022.

**Stockton Soccer Complex Playground & Food Truck Pad, Project No. CR15010**

Completed June 2023.

**Teen Impact Center Roof Replacement & Repairs, Project No. CR22002**

Replacement was completed in March 2022.

**Waterfront Lighting Restoration, Project No. WD22014**

Replacement was completed in May 2022.

# FINANCIAL SUMMARY

The tables below provide a quick summary of project budget and expenditure amounts to-date:

Project	Budget	Expenditures	Balance
<i>Projects in Construction</i>			
Brooking, Panella, Sandman, and Weber Park Playground Replacements, Project No. WP22026	\$1,000,000	\$286	\$999,714
Citywide Park Walkway Replacement, Project No. WP22015	\$150,000	\$50,868	\$99,132
Downtown Decorative Streetlight LED Conversion, Project No. WD22016	\$750,000	\$673,860	\$76,140
Intersection Safety Tree Trimming, Project No. WD22018	\$500,000	\$0	\$500,000
Miracle Mile RRFB & Improvements, Project No. WT22052	\$800,000	\$215,431	\$584,569
Pixie Woods Improvements, Project No. WP22054	\$1,100,000	\$6,040	\$1,093,960
Sidewalk Replacements, Project No. WD22053	\$4,000,000	\$268,603	\$3,731,397
Swimming Pool UV Sterilization System Improvements, Project No. WP22027	\$110,000	\$110,000	\$0
Tree Maintenance, Project No. WE22052	\$5,000,000	\$3,311,955	\$1,688,045
Van Buskirk Gym Floor Replacement, Project No. WC22003	\$300,000	\$271,568	\$28,432
Victory Park Tennis Court Lighting Refurbishment, Project No. WP22030	\$80,000	\$66,118	\$13,882
Weber Point Events Center Shade Structure Rehab, Project No. WP22033	\$1,250,000	\$170,115	\$1,079,885
SUBTOTAL	\$15,040,000	\$5,144,844	\$9,895,156

*See following page.*



Project	Budget	Expenditures	Balance
<b><i>Projects in Design</i></b>			
American Legion Park Lagoon Fencing Replacement, Project No. WP22036	\$150,000	\$0	\$150,000
Citywide Bridge Slope Protection, Project No. WT22039	\$300,000	\$227	\$299,773
Grupe Park Parking Lot Resurfacing, Project No. WD22011	\$500,000	\$92,142	\$407,858
Mattie Harrell Park Irrigation Well Replacement, Project No. WP22037	\$95,000	\$0	\$95,000
Oak Park Senior Center Parking Lot Resurfacing, Project No. WD22012	\$615,000	\$86,540	\$528,460
Pixie Woods Irrigation Automation, Project No. WP22038	\$80,000	\$6,482	\$73,518
Sousa Pool Crack Repair and Re-plastering, Project No. WP22040	\$200,000	\$16,456	\$183,544
Teen Impact Center Rehabilitation, Project No. CR22001	\$1,000,000	\$4,520	\$995,480
SUBTOTAL	\$2,940,000	\$206,367	\$2,733,633

Project	Budget	Expenditures	Balance
<b><i>Projects Completed</i></b>			
Downtown Abandoned Meter Pole Removals, Project No. WD22015	\$180,000	\$79,827	\$100,173
Fire Station 1 Renovations, Project No. F022002	\$100,000	\$100,000	\$0
Five Mile Creek Hyacinth Removal, Project No. WC22005	\$25,000	\$25,000	\$0
Gospel Center Rescue Mission Sidewalk Replacement, Project No. WD22017	\$240,000	\$201,013	\$38,987
Lower Sac Road Bridge at Mosher Slough Fence Replacement, Project No. WD22010	\$80,000	\$37,387	\$42,613
Oak Park Ball Field Improvements, Project No. WP22055	\$100,000	\$44,166	\$55,834
Pixie Woods Suspension Bridge Replacement, Project No. WP22039	\$120,000	\$27,827	\$92,173
Pixie Woods Tree Trimming & Brush Removal, Project No. WD22013	\$250,000	\$191,622	\$58,378
Stockton Soccer Complex Playground & Food Truck, Project No. CR15010	\$375,000	\$375,000	\$0
Teen Impact Center Roof Replacement & Structural Repairs, Project No. CR22002	\$900,000	\$290,934	\$609,066
Waterfront Lighting Restoration, Project No. WD22014	\$200,000	\$180,899	\$19,101
SUBTOTAL	\$2,570,000	\$1,553,675	\$1,016,325

<b>TOTAL</b>	<b>\$20,550,000</b>	<b>\$6,904,886</b>	<b>\$13,645,114</b>
--------------	---------------------	--------------------	---------------------

With closeout of the above projects, the Public Works Department will make a recommendation to the City Manager's Office for potential redistribution of project savings. As with all Capital Improvement Program projects, City Council approval is required to redistribute funds.
